




Start Date 30-Jul-19
Finish Date 17-Mar-20
Data Date 30-Jul-19
Run Date 23-Aug-19

- Remaining Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

KPCW Expansion
Big-D Construction
Preliminary Schedule

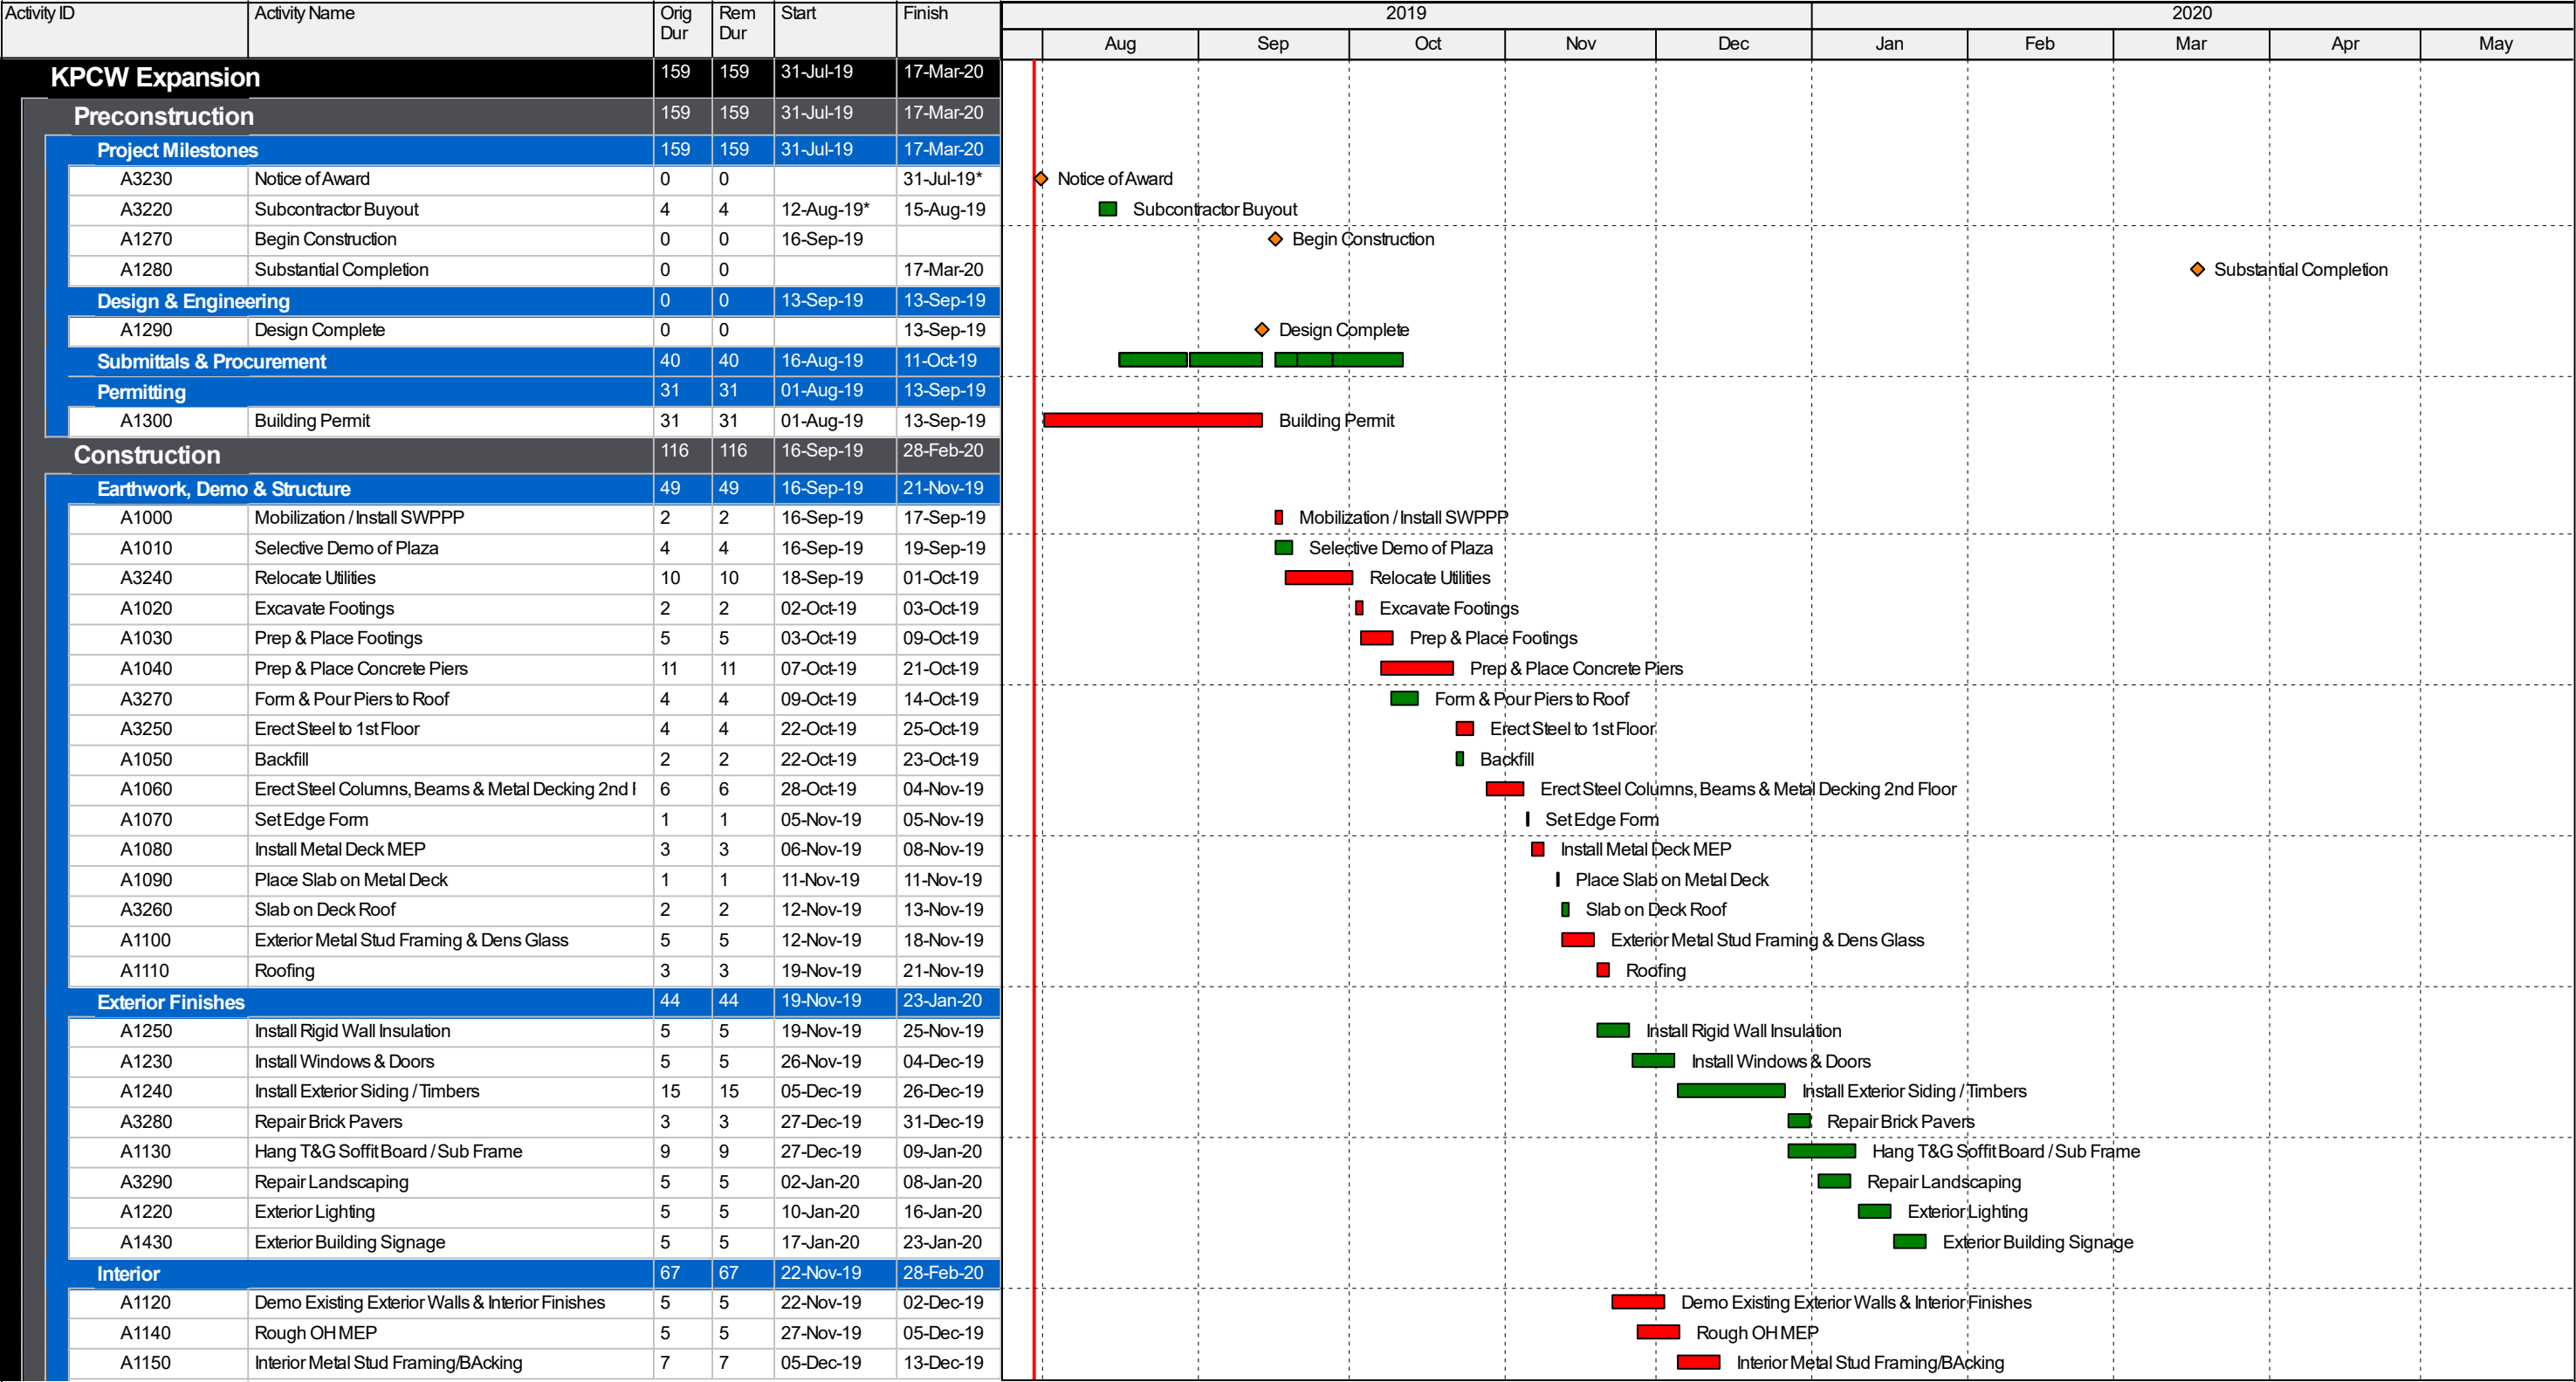

Activity ID		Activity Name	Orig Dur	Rem Dur	Start	Finish	2019						2020				
								Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
	A1200	Install Sound Isolation	3	3	11-Dec-19	13-Dec-19						■ Install Sound Isolation					
	A1160	Rough In-Wall MEP	8	8	16-Dec-19	26-Dec-19						■ Rough In-Wall MEP					
	A1170	Insulation	4	4	27-Dec-19	02-Jan-20						■ Insulation					
	A1180	4-Way Inspection	0	0		02-Jan-20						◆ 4-Way Inspection					
	A1210	install RC Channel	1	1	03-Jan-20	03-Jan-20						■ install RC Channel					
	A1190	Hang Drywall	4	4	06-Jan-20	09-Jan-20						■ Hang Drywall					
	A1310	Finish Drywall	8	8	10-Jan-20	21-Jan-20						■ Finish Drywall					
	A1320	Painting	5	5	22-Jan-20	28-Jan-20							■ Painting				
	A1340	Accoustical Ceiling Grid	5	5	29-Jan-20	04-Feb-20							■ Accoustical Ceiling Grid				
	A1400	Install Soundproof Glass	5	5	29-Jan-20	04-Feb-20							■ Install Soundproof Glass				
	A1410	Install Floor Tile	3	3	29-Jan-20	31-Jan-20							■ Install Floor Tile				
	A1330	Install Doors & Trim	5	5	03-Feb-20	07-Feb-20							■ Install Doors & Trim				
	A1380	Install Millwork & Countertops	5	5	10-Feb-20	14-Feb-20							■ Install Millwork & Countertops				
	A1350	Finish MEPS	5	5	17-Feb-20	21-Feb-20							■ Finish MEPS				
	A1390	Concrete Polishing	5	5	17-Feb-20	21-Feb-20							■ Concrete Polishing				
	A1360	Drop Tile	3	3	24-Feb-20	26-Feb-20							■ Drop Tile				
	A1420	Install Carpet Flooring	5	5	24-Feb-20	28-Feb-20							■ Install Carpet Flooring				
Closeout			12	12	02-Mar-20	17-Mar-20											
	A1440	Big-D Punchlist	5	5	02-Mar-20	06-Mar-20									■ Big-D Punchlist		
	A1450	A/E Punchlist	5	5	09-Mar-20	13-Mar-20									■ A/E Punchlist		
	A1460	Big-D Closeout	5	5	11-Mar-20	17-Mar-20									■ Big-D Closeout		
	A1470	CofO	0	0		17-Mar-20									◆ CofO		
	A1480	Substantial Completion	0	0		17-Mar-20									◆ Substantial Completion		
